

PROFESSIONAL TRAINING REPORT

Submitted in partial fulfillment of the requirements for the award of
Master of Architecture degree in Building Management

By

Albart A



SCHOOL OF BUILDING AND ENVIRONMENT
DEPARTMENT OF ARCHITECTURE
M. Arch (Building Management)

SATHYABAMA
INSTITUTE OF SCIENCE AND TECHNOLOGY
(DEEEMED TO BE UNIVERSITY)
Accredited with Grade 'A' by NAAC
JEPPIAR NAGAR, RAJIV GANDHI SALAI, CHENNAI - 600119

DEC- JAN 2020 - 21



SATHYABAMA

INSTITUTE OF SCIENCE AND TECHNOLOGY
(DEEMED TO BE UNIVERSITY)

(Est U/s(3) of UGC Act, 1956) Accredited with Grade "A" by NAAC (A Christian Minority Institution)

JEPPIAAR NAGAR, RAJIV GANDHI SALAI, CHEMMENCHERY, CHENNAI – 600119. TAMILNADU.

PHONE: 2450 1443/9941912481 INTERNET: www.sathyabama.ac.in

E-mail: archhod@sathyabama.ac.in



SCHOOL OF BUILDING AND ENVIRONMENT

DEPARTMENT OF ARCHITECTURE

M. Arch (Building management)

VIVA-VOCE EXAMINATION

This is to certify that the Professional Training (S84 INT) is the work of **Albart.A (39840003)** who had undergone training in **Urban Slab** and has been monitored by the continuous assessment during **Dec 2020 to Jan 2021**.

A handwritten signature in blue ink, which appears to read 'Devyani'.

Dr. Devyani Gangopadhyay
HOD AND DEAN

Submitted for Viva voce Examination held on _____

Internal Examiner

External Examiner



SATHYABAMA

INSTITUTE OF SCIENCE AND TECHNOLOGY
(DEEMED TO BE UNIVERSITY)

(Est U/s(3) of UGC Act,1956) Accredited with Grade "A" by NAAC (A Christian Minority Institution)

JEPPIAAR NAGAR, RAJIV GANDHI SALAI, CHEMMENCHERY, CHENNAI – 600119. TAMILNADU.

PHONE: 2450 1443/9941912481 INTERNET: www.sathyabama.ac.in

E-mail: archhod@sathyabama.ac.in



DECLARATION

I, **Albart.A (39840003)** hereby declare that the Professional Training Report 10th December 2020 to 20th January 2021 done by me under the guidance of **Ar.Immanuel** is submitted in partial fulfillment of the requirements for the completion of practical training session.

DATE : 20.01.2021

PLACE : Chennai



A. Albart
SIGNATURE OF CANDIDATE

ACKNOWLEDGEMENT

I am pleased to acknowledge my sincere thanks to Board of Management of **SATHYABAMA INSTITUTE OF SCIENCE & TECHNOLOGY** for their kind encouragement in doing this project and for completing it successfully. I am grateful to them.

I convey my thanks to **Dr.Devyani Gangopadhyay Dean, School of building and Environment** for providing me necessary support and details at the right time during the progressive reviews.

I would like to express my sincere and deep sense of gratitude to **Ar. Immanuel** for his valuable guidance, suggestions and constant encouragement paved way for the successful completion of my Training.

I would also like to express my sincere thanks to Ar. Sukirtha Suresh (Internal Co-Ordinator) for her valuable guidance, during the entire Professional Training period.

I wish to express my thanks to all Teaching and Non-teaching staff members of the Department of Architecture who were helpful in many ways for the completion of the project.

Also thank to the Principal Architect of the firm,

Ar.Immanuel,

Urban slab,

Anna Nagar, Chennai-40.



CONFIRMATION LETTER

(Annexure –V)



Urban **Slab**

To

07.12.2020

The Head of the Department

Department of Architecture, School of Building & Environment

Sathyabama Institute of Science and Technology

Rajiv Gandhi Salai, Jeppiaar Nagar.

Chennai-600 119, Tamil Nadu.

Sub: Confirmation letter for practical training at Urban Slab for A.Albart

Reg: 39840003

Respected sir,

With respect to the above subject we would like to induct **A.Albart (Reg: 39840003)** M.Arch in Building Management, Sathyabama Institute of science and technology, as a project management trainee for a period of **30 days** from **Dec 10th 2020 to January 20th 2021**.

Thanking you

Sincerely

Ar. Immanuel

Principal Architect,

Urban Slab, Chennai- 40

JOINING LETTER

(Annexure –VI)



Urban Slab

To 07.12.2020
The Head of the Department
Department of Architecture, School of Building & Environment
Sathyabama Institute of Science and Technology
Rajiv Gandhi Salai, Jeppiaar Nagar.
Chennai-600 119, Tamil Nadu.

Sub: Joining letter for practical training at Urban Slab for A.Albart Reg:
39840003

Respected sir,
We would like to congratulate **Albart.A (Reg: 39840003)** on being select-
ed for the "**Management Intern**" position, effective from 10.12.2020. This
internship will include training and focus primarily on learning and devel-
oping new skills.

Thanking you
Sincerely

Ar. Immanuel
Principal Architect,
Urban Slab, Chennai- 40

MONTHLY REPORT

(Annexure –VII)



SATHYABAMA
INSTITUTE OF SCIENCE AND TECHNOLOGY
(DEEMED TO BE UNIVERSITY)
(Est U/s(3) of UGC Act,1956) Accredited with Grade "A" by NAAC (A Christian Minority Institution)
JEPPIAAR NAGAR, RAJIV GANDHI SALAI, CHEMMENCHERY, CHENNAI – 600119. TAMILNADU.
PHONE: 2450 1443/9941912481 INTERNET: www.sathyabama.ac.in
E-mail: archhod@sathyabama.ac.in



DEPARTMENT OF ARCHITECTURE

M. Arch (Building management)

Continuous Assessment Report for Professional training

(Continuous progress report of the trainee architect/Project Manager for the period of 15 working days in the office to be submitted to HOD by the Trainee in Charge of the Organization)

1. Name of the office / organization : Urban Slab,
: #3,Bharani Apartments ,97 AG Block, 2nd Cross
Street Shanthi Colony, Annanagar, Chennai-600040.
Ph, +91 7904672288
2. Address & Contact Number
3. Name of the student : Albart. A
4. Duration : From 10.12.2020 To 31.12.2020
5. Total No. of days : 15

6. Evaluation of Performance criteria shall be on

* Note: Kindly grade the student as per his/her overall performance in the office during the assessment month; which will be converted to the allotted 40 marks by the department.


Description of works	Excellent	Good	Fair	Poor	NA
Understanding of office culture	✓				
Skillsets related to project management	✓				
Design Management		✓			
Understanding the Triple Constraints		✓			
Observation during Site Visits	✓				
Understanding of construction details	✓				
Understanding of Construction sequences	✓				
Site Supervision / Discussion with clients		✓			
Adherence to Time schedule		✓			
Quantitative aptitude	✓				
Documentation skills		✓			
Coordination with other consultants	✓				

Overall Grading*

(A – 8.0, B – 7.0, C – 6.0, D – 5.5, E – 5.0, F – <5)

7. Any other Remarks

8. Signature of the
Head of the Office /
Organization (With Seal)



SATHYABAMA
INSTITUTE OF SCIENCE AND TECHNOLOGY
(DEEMED TO BE UNIVERSITY)
(Est U/s(3) of UGC Act,1956) Accredited with Grade "A" by NAAC (A Christian Minority Institution)
JEPPIAAR NAGAR, RAJIV GANDHI SALAI, CHEMMENCHERY, CHENNAI – 600119. TAMILNADU.
PHONE: 2450 1443/9941912481 INTERNET: www.sathyabama.ac.in
E-mail: archhod@sathyabama.ac.in



M. Arch (Building management)

Continuous Assessment Report for Professional training

(Continuous progress report of the trainee architect/Project Manager for the period of 15 working days in the office to be submitted to HOD by the Trainee in Charge of the Organization)

1. Name of the office / organization : Urban Slab,
: #3,Bharani Apartments ,97 AG Block, 2nd Cross
Street Shanthi Colony, Annanagar, Chennai-600040.
Ph, +91 7904672288
2. Address & Contact Number
3. Name of the student : Albart. A
4. Duration : From 01.01.2021 To 20.01.2021
5. Total No. of days : 15
6. Evaluation of Performance criteria shall be on

* Note: Kindly grade the student as per his/her overall performance in the office during the assessment month; which will be converted to the allotted 40 marks by the department.

Description of works	Excellent	Good	Fair	Poor	NA
Understanding of office culture	✓				
Skillsets related to project management	✓				
Design Management		✓			
Understanding the Triple Constraints		✓			
Observation during Site Visits	✓				
Understanding of construction details	✓				
Understanding of Construction sequences		✓			
Site Supervision / Discussion with clients		✓			
Adherence to Time schedule	✓				
Quantitative aptitude	✓				
Documentation skills	✓				
Coordination with other consultants	✓				

Overall Grading*

(A – 8.0, B – 7.0, C – 6.0, D – 5.5, E – 5.0, F – <5)

7. Any other Remarks

8. Signature of the
Head of the Office /
Organization (With Seal)



WORK DIARY

(Annexure -VIII)

DAY	PROJECT NAME	WORK DONE	DAY	PROJECT NAME	WORK DONE
1	Sekar Residency	Scheduling	16	Gobi Residency	Site visit
2	Sekar Residency	Scheduling.	17	Gobi Residency	Site visit
3	Sekar Residency	Scheduling.	18	Gobi Residency	Site visit
4	Sekar Residency	Scheduling.	19	Gobi Residency	Site visit
5	Sekar Residency	Scheduling.	20	Gobi Residency	Site visit
6	Narin Residency	Site Inspection	21	Samy Residency	Scheduling
7	Narin Residency	Site Inspection	22	Samy Residency	Scheduling
8	Narin Residency	Site Inspection	23	Venkat Residency	Site visit
9	Samy Residency	Scheduling	24	Venkat Residency	Site visit
10	Samy Residency	Scheduling	25	Gobi Residency	Site visit
11	Samy Residency	Scheduling.	26	Gobi Residency	Site visit
12	Samy Residency	Scheduling.	27	Venkat Residency	Site visit
13	Samy Residency	Scheduling	28	Venkat Residency	Site visit
14	Samy Residency	Scheduling	29	Venkat Residency	Site visit
15	Samy Residency	Scheduling.	30	Venkat Residency	Site visit.

Chief Architect Signature:

Office seal:



Consolidated Certificate (Experience)

Annexure – IX



Urban **Slab**

To

20.01.2021

The Head of the Department

Department of Architecture, School of Building & Environment

Sathyabama Institute of Science and Technology

Rajiv Gandhi Salai, Jeppiaar Nagar.

Chennai-600 119, Tamil Nadu.

Sub: Completion letter for practical training at Urban Slab for A.Albart

Reg: 39840003

Respected sir,

This is to certify that **A.Albart (Reg: 39840003)** has undergone project management student training with us from **10.12.2020 to 20.01.2021** and had successfully completed the **30 days** period training. During his tenure as a trainee with us we found him to be diligent, intelligent and hard work. We wish him all the best and success for the future endeavors. He has been relieved from all his services as per the rule of the company.

Thanking you

Sincerely

Ar. Immanuel
Principal Architect,
Urban Slab, Chennai- 40



INTRODUCTION

ABOUT THE FIRM:

URBAN SLAB is a design based Firm in Chennai, Tamil Nadu. URBAN SLAB offers varied services on different platforms.

IDEALOGY THE FIRM:

- Social relationship enhancement
- Creativity
- Execution
- Thinner – Lighter – Economical
- Affordability without compromising comfort
- Positivity - Inter and Intra company
- Create and spread Energy
- Equality and Diversity

OBJECTIVES OF PROFFESIONAL TRAINING:

The main objectives of the professional training is

- To understand the role of project management in construction industry
- Contributions of the firm to the project
- To explore the core areas of Building services and management
- To learn about the business side of the things

SECTORS OF OPERATION

- **Operations and Allied services**
 - Project Management
 - Business Development
- **Architectural and Allied services**
 - General Architecture
 - Landscape Architecture
 - Interior Design
 - Environmental Solution

PROJECT – 1

Mr.Sekar Residence

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 1, 2019 J F M A M J	Half 2, 2019 J A S O N D	Half 1, 2020 J F M A M J	Half 2, 2020 J A S O N D	Half 1, 2021 J F M A
1		Medavakkam Residence	38 days	Mon 18-01-21	Tue 02-03-21						
2		Renovation work	35 days	Mon 18-01-21	Fri 26-02-21						
3		Civil work	24 days	Mon 18-01-21	Sat 13-02-21						
4		Removal of Terrace existing weathering tile layer	3 days	Mon 18-01-21	Wed 20-01-21						
5		Wall Demolition and Fixing of grill gate and Flush door at First Floor Home Office entry	2 days	Thu 21-01-21	Fri 22-01-21	19FF					
6		Platform work For staircase at parking space	1 day	Thu 21-01-21	Thu 21-01-21	4					
7		Removal of existing kitchen slab and Dado tile (granite and pipe lines)	2 days	Thu 21-01-21	Fri 22-01-21	4					
8		Removal of existing utility slab and relaying new pipe lines	2 days	Tue 02-02-21	Wed 03-02-21						
9		Re-fixing of new granite and fixtures as per the client selection	2 days	Fri 12-02-21	Sat 13-02-21	8					
10		Re-fixing of new toilet fixtures as per the client selection	2 days	Mon 08-02-21	Tue 09-02-21	16					
11		Sump tank Cover work	4 days	Thu 04-02-21	Mon 08-02-21	8					
12		Touch up work and replacing IC box cover tile	1 day	Tue 09-02-21	Tue 09-02-21	11					
13		Tile work	18 days	Thu 21-01-21	Wed 10-02-21						
14		New weathering tile work on terrace	4 days	Thu 21-01-21	Mon 25-01-21	4					
15		Master Toilet Tile work	3 days	Tue 02-02-21	Thu 04-02-21						
16		Ground floor Toilet Tile work	2 days	Fri 05-02-21	Sat 06-02-21	15					
17		Kitchen and Utility dado tile work as per the client selection	3 days	Mon 08-02-21	Wed 10-02-21	33					
18		MS Fabrication work	16 days	Fri 22-01-21	Tue 09-02-21						
19		Office entry grill work	1 day	Fri 22-01-21	Fri 22-01-21	6					
20		Front staircase work	4 days	Sat 23-01-21	Wed 27-01-21	19					
21		Terrace ladder work	2 days	Tue 26-01-21	Wed 27-01-21	20FF					
22		Finishing works	1 day	Tue 02-02-21	Tue 02-02-21						
23		Painting work	2 days	Mon 08-02-21	Tue 09-02-21						
24		Painting work	6 days	Sat 20-02-21	Fri 26-02-21						
25		Office room touch up work	1 day	Sat 20-02-21	Mon 22-02-21	26SF					
26		Kitchen and Utility painting work (touch up putty, 2 coats of paint)	3 days	Mon 22-02-21	Wed 24-02-21	38					
27		Polishing wooden partition stand	2 days	Thu 25-02-21	Fri 26-02-21	26					
28		Carpentry work	28 days	Wed 20-01-21	Sat 20-02-21						
29		Removal of all Shutters from kitchen	1 day	Wed 20-01-21	Wed 20-01-21	4FF					
30		Master Wardrobe Wood work box type	3 days	Tue 02-02-21	Thu 04-02-21	29					
31		First floor Frensh Window replacement work	1 day	Sat 23-01-21	Sat 23-01-21	5					
32		Kitchen box work	6 days	Fri 05-02-21	Thu 11-02-21	30					
33		Utility box work	2 days	Fri 05-02-21	Sat 06-02-21	30					
34		Ground floor Consultancy storage Box work	1 day	Mon 08-02-21	Mon 08-02-21	33					
35		Tv unit Work	1 day	Tue 09-02-21	Tue 09-02-21	34					
36		Bedroom loft work	3 days	Wed 10-02-21	Fri 12-02-21	35					
37		Factory order for all shutters	7 days	Tue 09-02-21	Tue 16-02-21	34					
38		Shutters fixing work for Kitchen, Utility, Consultancy room, master wardrobe	4 days	Wed 17-02-21	Sat 20-02-21	37					

Project: C:\Users\DELL\Desktop Date: Sat 30-01-21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

PROJECT – 1

Mr.Sekar Residence

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 1, 2019 J F M A M J	Half 2, 2019 J A S O N D	Half 1, 2020 J F M A M J	Half 2, 2020 J A S O N D	Half 1, 2021 J F M A
39			Terrace floor storage rack	2 days	Tue 09-02-21	Wed 10-02-21	34					
40			All windows and doors recheck	2 days	Thu 11-02-21	Fri 12-02-21	39					
41			False Ceiling work	3 days	Mon 08-02-21	Wed 10-02-21						
42			False Ceiling work at home office	3 days	Mon 08-02-21	Wed 10-02-21						
43			Electrical work	11 days	Tue 02-02-21	Sat 13-02-21						
44			Electrician inspection	1 day	Tue 02-02-21	Tue 02-02-21						
45			Rechecking lines and rectifying it	2 days	Mon 08-02-21	Tue 09-02-21	44FS+4 days					
46			Kitchen and utility electrical work	2 days	Wed 10-02-21	Thu 11-02-21	45					
47			Refixting the applilances as per the client requirments	2 days	Fri 12-02-21	Sat 13-02-21	46					
48			CLOSURE	3 days	Sat 27-02-21	Tue 02-03-21						
49			Testing and quality check	2 days	Sat 27-02-21	Mon 01-03-21	27					
50			Closure documents	1 day	Tue 02-03-21	Tue 02-03-21	49					

Project: C:\Users\DELL\Desktop Date: Sat 30-01-21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

PROJECT – 2
Mr.Navin Residence



PROJECT – 3

Mr.Samy Residence

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 1, 2019 J F M A M J	Half 2, 2019 J J A S O N D	Half 1, 2020 J F M A M J	Half 2, 2020 J J A S O N D	Half 1, 2021 J F M A M
1		Kundrathur Residence	70 days	Wed 20-01-21	Sat 10-04-21						
2		Renovation work	67 days	Wed 20-01-21	Wed 07-04-21						
3		Civil work	22 days	Wed 20-01-21	Sat 13-02-21						
4		Removal of existing compound wall	1 day	Wed 20-01-21	Wed 20-01-21						
5		Removal of existing parking tiles and staircase tiles	2 days	Thu 21-01-21	Fri 22-01-21	4					
6		Removal of front entrance grill work as per the design	1 day	Thu 21-01-21	Thu 21-01-21	4					
7		Removal of existing kitchen counter and tile work on study room	2 days	Thu 21-01-21	Fri 22-01-21	4					
8		Removal of existing common toilet tiles and plumbing lines and relaying as per the design	3 days	Tue 02-02-21	Thu 04-02-21	7					
9		Removing of master bedroom toilet tiles and relaying plumbing lines as per the design	2 days	Fri 12-02-21	Sat 13-02-21	7					
10		Removal of brick wall on the master bedroom inner area for new opening from inside and closing the existing opening	2 days	Fri 05-02-21	Sat 06-02-21	8					
11		Water proofing for all the toilets	1 day	Fri 05-02-21	Fri 05-02-21	8					
12		Removal of existing kitchen counters	1 day	Sat 06-02-21	Sat 06-02-21	11					
13		Removal of existing storage slabs in kitchen for boxing work	1 day	Sat 06-02-21	Sat 06-02-21	11					
14		Removal of existing brick wall for new opening on two sides as per the design	1 day	Mon 08-02-21	Mon 08-02-21	12					
15		Removal of master bedroom and kitchen door frame	1 day	Mon 08-02-21	Mon 08-02-21	12					
16		Plumbing work for kitchen and utility area as per the design	1 day	Tue 09-02-21	Tue 09-02-21	15					
17		Removal of existing slab in the living area for newly proposed seating area	1 day	Tue 09-02-21	Tue 09-02-21	15					
18		Weathering work for terrace (traditional method)	3 days	Mon 08-02-21	Wed 10-02-21	10					
19		Headroom sheeting brick work	2 days	Thu 11-02-21	Fri 12-02-21	18					
20		Tile work	14 days	Sat 13-02-21	Mon 01-03-21						
21		New weathering tile work on terrace	3 days	Sat 13-02-21	Tue 16-02-21	19					
22		Relaying new parking tile as per the client selection	2 days	Wed 17-02-21	Thu 18-02-21	21					
23		Laying tile for steps	2 days	Fri 19-02-21	Sat 20-02-21	22					
24		Laying floor tiles in study area	1 day	Mon 22-02-21	Mon 22-02-21	23					
25		Master Toilet Tile work	2 days	Tue 23-02-21	Wed 24-02-21	24					
26		Commom Toilet Tile work	2 days	Thu 25-02-21	Fri 26-02-21	25					
27		Kitchen and Utility dado tile work as per the client selection	2 days	Sat 27-02-21	Mon 01-03-21	26					
28		MS Fabrication work	19 days	Fri 22-01-21	Fri 12-02-21						
29		Parking ms gate work with WBC Board	1 day	Fri 22-01-21	Fri 22-01-21	6					
30		Pedestrian gate work	4 days	Sat 23-01-21	Wed 27-01-21	29					
31		Front fixed grill work with openable door (safety gate)	2 days	Thu 28-01-21	Fri 29-01-21	30					
32		Staircase handrail work	1 day	Tue 02-02-21	Tue 02-02-21	31					
33		Headroom sheet work	2 days	Mon 08-02-21	Tue 09-02-21	32					
34		Terrace seat out area sheeting work	3 days	Wed 10-02-21	Fri 12-02-21	33					
35		Painting work	31 days	Sat 13-02-21	Sat 20-03-21						

Project: C:\Users\DELL\Desktop
Date: Sat 30-01-21

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

PROJECT – 3

Mr.Samy Residence

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 1, 2019 J F M A M J	Half 2, 2019 J A S O N D	Half 1, 2020 J F M A M J	Half 2, 2020 J A S O N D	Half 1, 2021 J F M A M
36			External painting	18 days	Sat 13-02-21	Fri 05-03-21						
37			Cleaning of exterior wall for new painting work	4 days	Sat 13-02-21	Wed 17-02-21	34					
38			1 coat of primer	5 days	Thu 18-02-21	Tue 23-02-21	37					
39			2 coats of exterior paint	5 days	Wed 24-02-21	Mon 01-03-21	38					
40			Exterior grill painting work	4 days	Tue 02-03-21	Fri 05-03-21	39					
41			Internal painting	13 days	Sat 06-03-21	Sat 20-03-21						
42			Touch putty work	4 days	Sat 06-03-21	Wed 10-03-21	40					
43			Cleaning of wall for painting	4 days	Thu 11-03-21	Mon 15-03-21	42					
44			2 coats of paint as per the client selection	5 days	Tue 16-03-21	Sat 20-03-21	43					
45			Carpentry work	31 days	Tue 09-02-21	Tue 16-03-21						
46			Kitchen bottom cabinet and upper cabinet work	5 days	Tue 09-02-21	Sat 13-02-21	14					
47			Kitchen loft work (frame and shutter)	1 day	Mon 15-02-21	Mon 15-02-21	46					
48			Kitchen storage unit	1 day	Tue 16-02-21	Tue 16-02-21	47					
49			Utility sink bottom cabinet work	2 days	Tue 16-02-21	Wed 17-02-21	47					
50			Dining cutlery unit	2 days	Tue 16-02-21	Wed 17-02-21	47					
51			Dining wash basin bottom cabinet work	1 day	Tue 09-02-21	Tue 09-02-21	14					
52			Master bedroom loft work (frame and shutter)	1 day	Wed 10-02-21	Wed 10-02-21	51					
53			New Wardrobe work in master bedroom	2 days	Thu 11-02-21	Fri 12-02-21	52					
54			New Wardrobe work in bedroom 1	1 day	Sat 13-02-21	Sat 13-02-21	53					
55			Bedroom 1 loft work (frame and shutter)	1 day	Mon 15-02-21	Mon 15-02-21	54					
56			Carpentry for book rack in study area (frame and shutter)	2 days	Tue 16-02-21	Wed 17-02-21	55					
57			Tv unit carpentry work	4 days	Thu 18-02-21	Mon 22-02-21	56					
58			Dewan seating carpentry work with storage	2 days	Tue 23-02-21	Wed 24-02-21	57					
59			Pooja unit carpentry work with storage	2 days	Thu 25-02-21	Fri 26-02-21	58					
60			Shoe rack carpentry work with seating area	2 days	Thu 25-02-21	Fri 26-02-21	58					
61			Factory order for all shutters	7 days	Sat 27-02-21	Sat 06-03-21	60					
62			Shutters fixing work for all wood works	8 days	Mon 08-03-21	Tue 16-03-21	61					
63			All windows and doors recheck	2 days	Sat 27-02-21	Mon 01-03-21	60					
64			False Ceiling work	4 days	Sat 27-02-21	Wed 03-03-21						
65			False Ceiling work at Living space	4 days	Sat 27-02-21	Wed 03-03-21	60					
66			Electrical work	15 days	Mon 22-03-21	Wed 07-04-21						
67			Electrician inspection	1 day	Mon 22-03-21	Mon 22-03-21	44					
68			Rechecking lines and rectifying it	4 days	Sat 27-03-21	Wed 31-03-21	67FS+4 days					
69			Electrical work for all wood works	4 days	Thu 01-04-21	Mon 05-04-21	68					
70			Refixing the applilances as per the client requirments	2 days	Tue 06-04-21	Wed 07-04-21	69					
71			CLOSURE	3 days	Thu 08-04-21	Sat 10-04-21						
72			Testing and quality check	2 days	Thu 08-04-21	Fri 09-04-21	70					
73			Closure documents	1 day	Sat 10-04-21	Sat 10-04-21	72					

Project: C:\Users\DELL\Desktop
Date: Sat 30-01-21

Task

Split

Milestone

Summary









Project Summary

Inactive Task

Inactive Milestone

Inactive Summary









Manual Task

Duration-only

Manual Summary Rollup

Manual Summary









Start-only

Finish-only

External Tasks

External Milestone









Deadline

Progress

Manual Progress








PROJECT – 4
Mr.Gobi Residence



PROJECT – 5
Mr. Venkat Residence

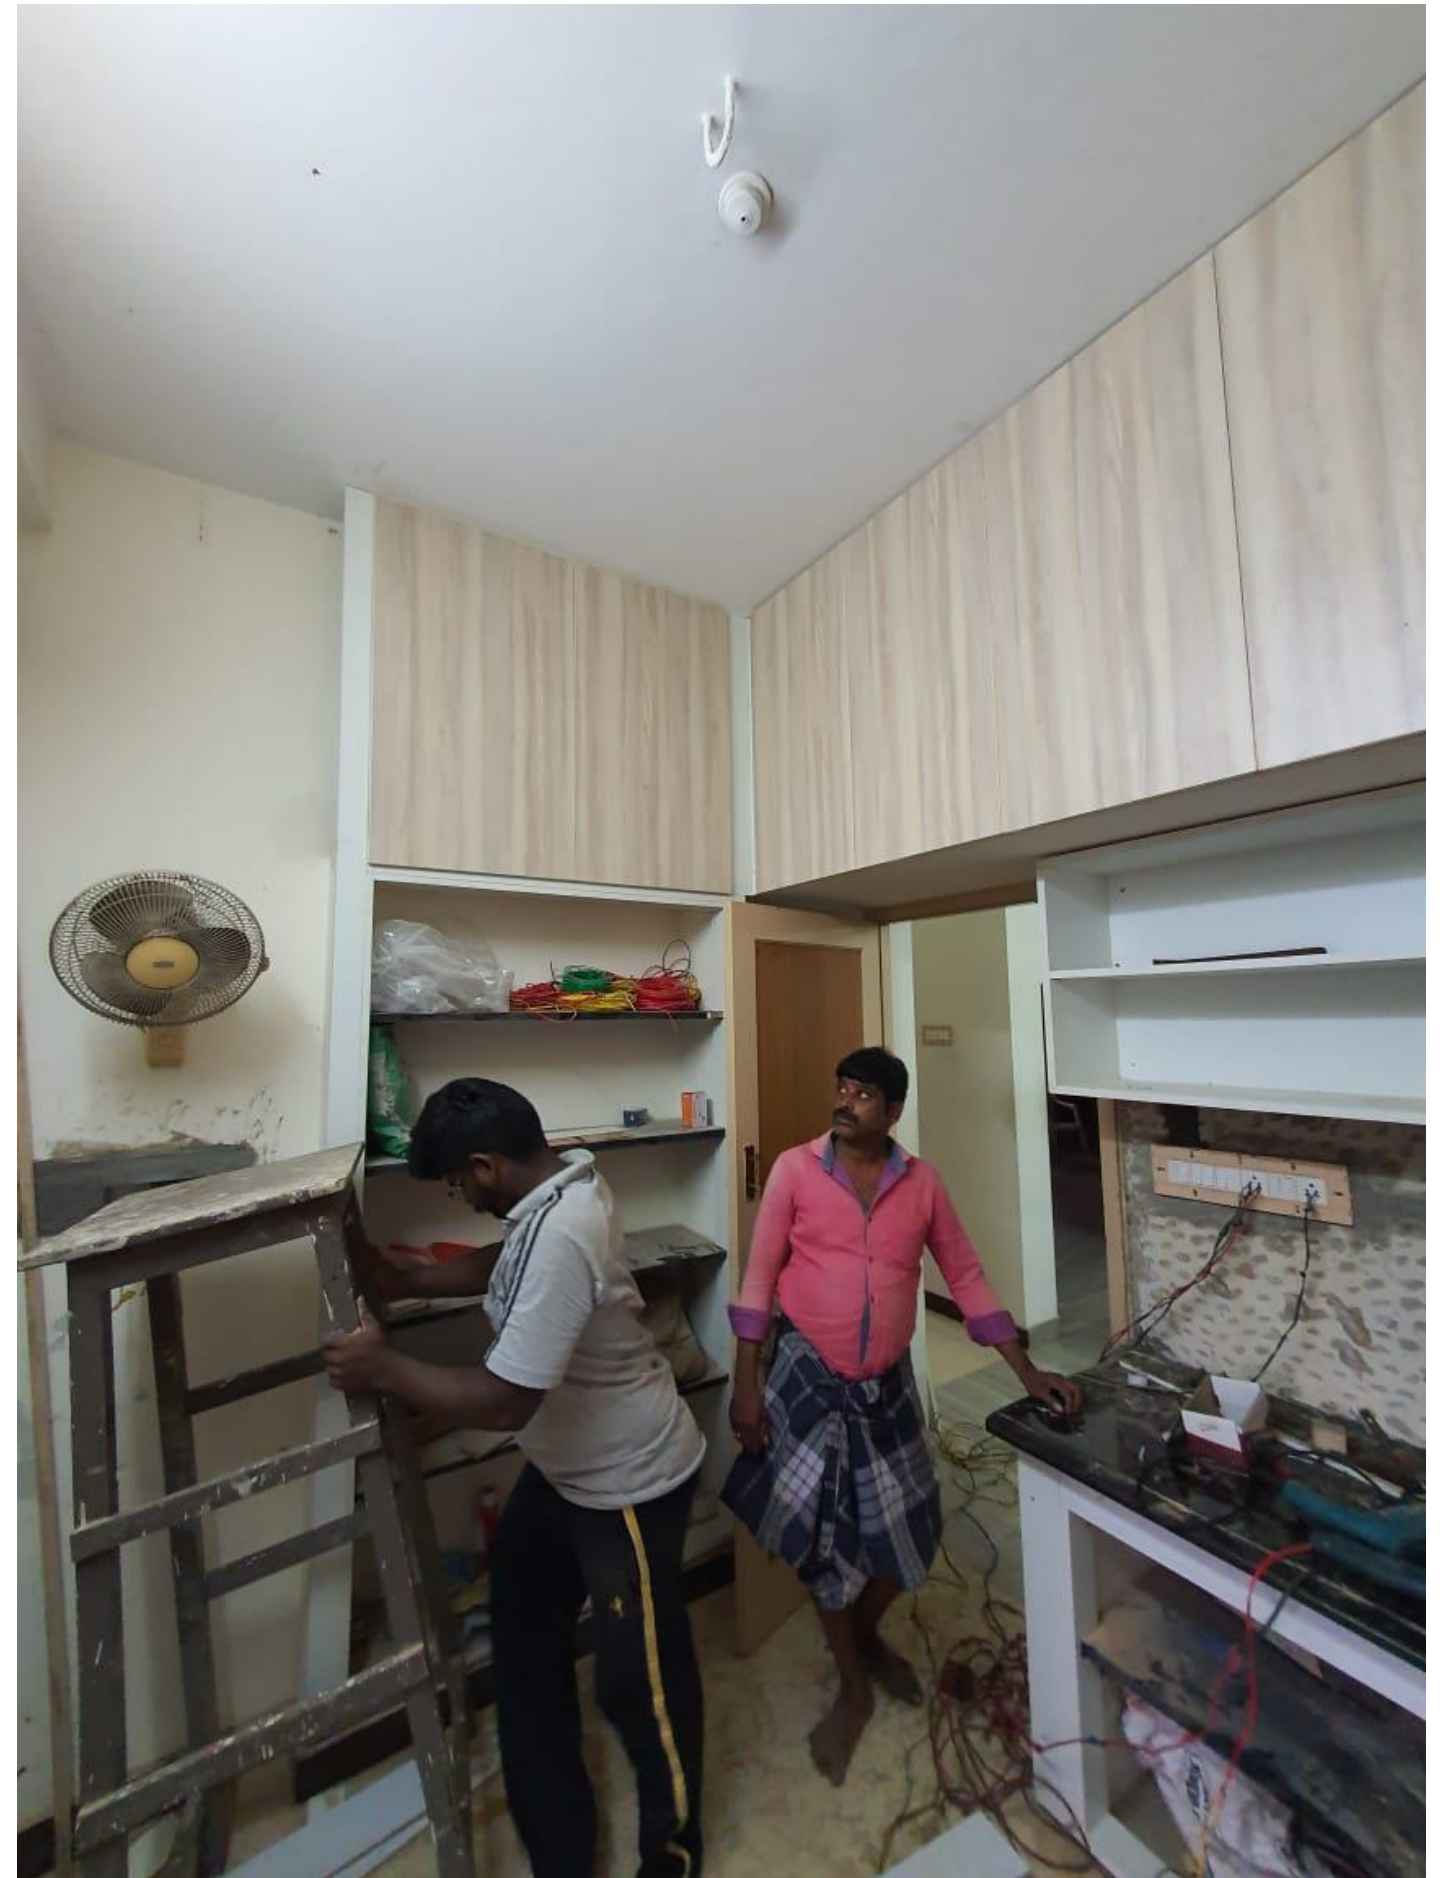

Thank you..
